

Accessibility Checklist

13 Jun 2025 / Winona Ritchie

Complete

Score	36 / 37 (97.3%)	Flagged items	1	Actions	1
Date				13	Jun 2025 07:00 PST
Inspector N	ame				Winona Ritchie
Facility Type	e			Manufa	acturing Warehouse
Location				(21.391	Pearl City, HI, USA 0364, -157.9715193)

Flagged items & Actions

1 flagged, 1 action

Flagged items

1 flagged, 1 action

Restrooms & Employee Facilities

Are restrooms equipped with at least one accessible stall with grab bars installed per ADA guidelines?



The employee restroom on the second floor does not have an accessible grab bar.



Photo 1

To do | Assignee: SafetyCulture Staff | Priority: High | Due: 10 Jul 2025 07:15 PST | Created by: SafetyCulture Staff

Lack of grab bar in employee restroom.

Action needed on noncompliant restroom feature

Other actions 0 actions

Accessible Parking & Exterior Access	6 / 6 (100%)
Are accessible parking spaces provided with correct dimensions and located closest to accessible entrances?	Yes
Are access aisles adjacent to accessible parking spaces level, marked "No Parking," and wide enough for wheelchair access?	Yes
Are accessible routes from parking to building entrances firm, stable, slip-resistant, and at least 36 inches wide?	Yes
Are curb ramps or ramps with compliant slope, handrails, edge protection, and proper landings provided where needed?	Yes
Are exterior walkways free of obstructions, hazards, and well-maintained?	Yes
Is exterior signage for accessible parking and routes clear, visible, and compliant with ADA requirements?	Yes

Entrances & Doorways	6 / 6 (100%)
Is there at least one accessible entrance with a minimum clear width of 32 inches?	Yes
Are door thresholds beveled and no higher than ½ inch to allow smooth wheelchair passage?	Yes
Is door hardware accessible (lever handles, push plates) and operable without tight grasping, pinching, or twisting?	Yes
Are maneuvering clearances provided on both sides of doors per ADA standards?	Yes
Are automatic or power-assisted doors installed where feasible to improve accessibility?	Yes
Are entrance doors maintained in good working order, free of damage or obstructions?	Yes

Interior Routes & Circulation	6 / 6 (100%)
Are all primary interior routes, corridors, and aisles at least 36 inches wide and free of obstructions?	Yes
Are floor surfaces firm, stable, and slip-resistant throughout accessible routes?	Yes
Are turning spaces (minimum 60-inch diameter or T-shaped) provided at key points for wheelchair users?	Yes
Are thresholds inside the building beveled and low enough to allow easy passage?	Yes
Are interior doors accessible with proper clear widths and maneuvering space?	Yes
Are ramps inside the building compliant with slope, handrails, and landing requirements?	Yes

Restrooms & Employee Facilities

1 flagged, 1 action, 4 / 5 (80%)

Are restrooms equipped with at least one accessible stall with grab bars installed per ADA guidelines?



The employee restroom on the second floor does not have an accessible grab bar.



Photo 1

To do | Assignee: SafetyCulture Staff | Priority: High | Due: 10 Jul 2025 07:15 PST | Created by: SafetyCulture Staff

Lack of grab bar in employee restroom.

Action needed on noncompliant restroom feature

Are sinks accessible with knee clearance and operable faucets?	Yes
Are restroom doors wide enough and equipped with accessible hardware?	Yes
Are break rooms, locker rooms, and other employee facilities accessible with clear floor space and reachable amenities?	Yes
Are drinking fountains or water dispensers accessible with proper clear floor space?	N/A
Are restrooms and employee facilities maintained clean and in good working order?	Yes

Signage & Wayfinding	5 / 5 (100%)
Is signage for accessible routes, entrances, restrooms, and emergency exits clear, visible, and easy to understand?	Yes
Is tactile and Braille signage installed where required on room and directional signs?	N/A
Are signs mounted at accessible heights (typically 48 to 60 inches above the floor)?	Yes
Are signs illuminated or placed in well-lit areas for visibility?	Yes
Are safety and hazard signs posted and legible throughout the facility?	Yes
Are wayfinding signs consistent in design and placement to assist all users?	Yes

Emergency Access & Safety	3 / 3 (100%)
Are emergency exits accessible, unobstructed, and clearly identified?	Yes
Are emergency alarms both audible and visual?	Yes
Is an emergency evacuation plan posted and communicated?	Yes

General Safety & Maintenance	6 / 6 (100%)
Are floors and pathways free of hazards such as spills, debris, or tripping risks?	Yes
Is lighting adequate throughout the facility to ensure safe navigation and task performance?	Yes
Are maintenance and housekeeping practices sufficient to maintain clear and accessible routes?	Yes
Are emergency equipment and safety devices (e.g., fire extinguishers, first aid kits) regularly inspected and accessible?	Yes
Are all floor mats, rugs, and coverings securely fastened to prevent slipping or tripping?	Yes
Are signs of wear, damage, or deterioration on floors, walls, doors, and handrails promptly identified and repaired?	Yes

Sign Off

Briefly summarize any major accessibility issues found, corrective actions needed, or general observations.

Summary of Findings

Warehouse facility generally adheres to accessibility standards. However, action is needed to address the issue in the employee restroom and provide the proper grab bars for better inclusivity. Please see assigned action.

Inspector Name and Signature

Winona Ritchie Winona Ritchie 3 Jul 2025 07:18 PST

Media summary

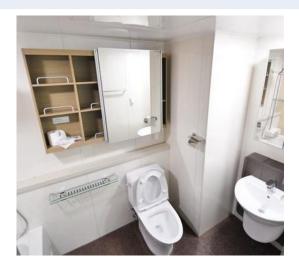


Photo 1
